Lake Dallas CTE - Theatre Lighting, Theatre Rigging Punch List

Created: 10-27-2025
Creator: Jeff Mabray (@JMA)
Status: Missing, Not Installed, Not Complete, Incorrect, Unable To Inspect
Dates: 07-18-2025 - 10-27-2025

Recipients

VLK Architects, Crossland Construction

Description

WJHW representatives made a site visit on 10/10/25. While on site we met with Crossland General Contractors.

Items identified in this report are a reflection of site conditions during that site visit. These observations do not relieve the contractors from any requirements of the contract documents.

Items in the report are typically noted as being in a particular status:
Missing - This means that the item was not found and needs to be installed.

Not Installed - Used for items where there is infrastructure in place, but the installation of the item (i.e. the DB) has not been completed.

Not Complete - Used for items where things generally look ok so far, but the system is not complete. (i.e. The DB and infrastructure is in place, but the Display is not installed yet)

Incorrect: The item is installed - but it is not correct in how it is installed.


Unable to Inspect: We were unable to view and/or test a particular item, either due to lack of access or uncontrollable site conditions.

Please note: When viewing each task, you are welcome to click on the picture to enlarge it as required.

Architectural Lighting


#33 - EC still working on circuiting and arch. fixtures.

Not Complete | Chris Purpura | Architectural Lighting
Plan: 2-TL2-21B1 - FLOOR PLAN - FA MEZZANINE LEVEL - UNIT B-1
Created 10-10-2025

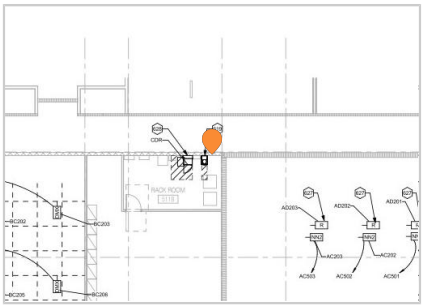

Task messages (time in CDT)

Chris Purpura

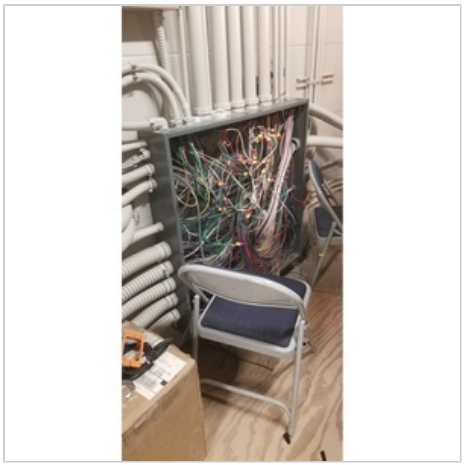

10 Oct 07:20 PM

Chris Purpura


EC still working on circuiting and arch. fixtures.

10 Oct 07:21 PM

Theatrical Lighting

#9 - PB and DMX Devices Not Installed

Not Complete | Alex Robertson | Theatrical Lighting
Plan: 2-TL2-11C1 - FLOOR PLAN - LOWER LEVEL - UNIT C-1
Created 07-22-2025

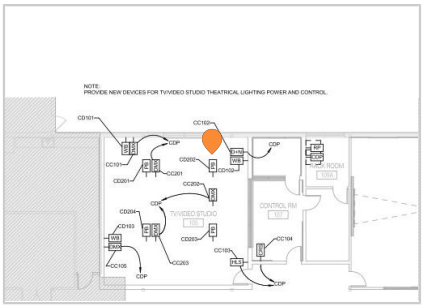


Task messages (time in CDT)

Alex Robertson	no pipe grid has been installed in the studio.	22 Jul 10:47 AM
Chris Purpura	PB & DMX devices not complete & tested. Finish programming and labeling ETC - Complete	ct 06:05 PM
Chris Purpura		10 Oct 06:10 PM
Chris Purpura	Install plates on preset stations and finish programming. ETC - Complete	10 Oct 06:10 PM

#10 - RP and CDP Devices Not Installed

Not Complete | Alex Robertson | Theatrical Lighting
Plan: 2-TL2-11C1 - FLOOR PLAN - LOWER LEVEL - UNIT C-1
Created 07-22-2025

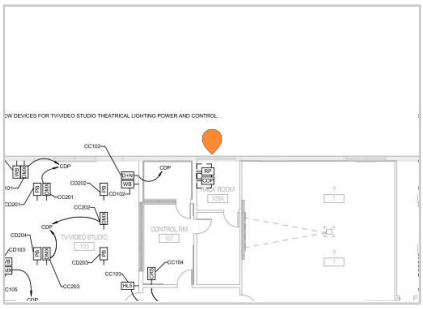


Task messages (time in CDT)

Alex Robertson	The RP and CDP devices were not installed or conduit ran into rack room. No electrical circuits have been identified to power either device.	22 Jul 10:49 AM
Chris Purpura	Finish labeling CDP. Overall system not working, finish programming. ETC - Complete	10 Oct 06:09 PM

#22 - Provide labelling for the CDP. Finish labeling of the cables to match the as-builts.

Not Complete | Chris Purpura | Theatrical Lighting
Plan: 2-TL2-11B1 - FLOOR PLAN - MAIN LEVEL - UNIT B-1
Created 10-10-2025

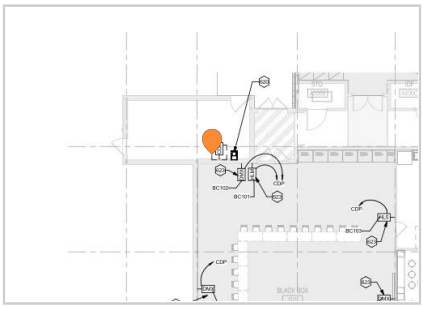


Task messages (time in CDT)

Chris Purpura	Provide labelling for the CDP. Finish labeling of the cables to match the as-builts.	10 Oct 06:14 PM

ETC - Complete

#23 - Provide cover over existing preset station.

Not Complete | Chris Purpura | Theatrical Lighting
Plan: 2-TL2-11B1 - FLOOR PLAN - MAIN LEVEL - UNIT B-1
Created 10-10-2025

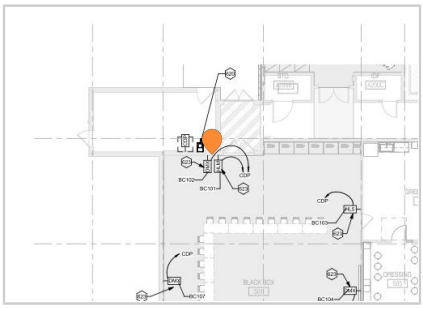

Task messages (time in CDT)

Chris Purpura




10 Oct 06:15 PM

Chris Purpura — Provide cover over existing preset station. ETC - Out of Scope — 10 Oct 06:15 PM

#24 - Install plates on all HL presets in auditorium (typical). Finish programming on all preset stations.

Not Complete | Chris Purpura | Theatrical Lighting
Plan: 2-TL2-11B1 - FLOOR PLAN - MAIN LEVEL - UNIT B-1
Created 10-10-2025

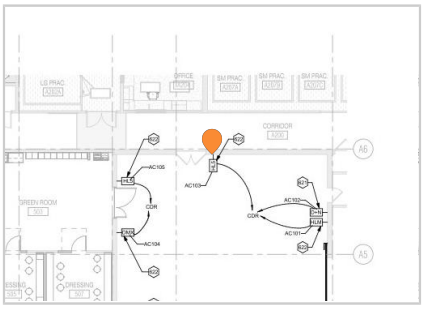


Task messages (time in CDT)

Chris Purpura		10 Oct 06:17 PM
Chris Purpura	Install plates on all HL presets in auditorium (typical). Finish programming on all preset stations. ETC - Complete	10 Oct 06:18 PM

#25 - Install plates on all HL presets in auditorium (typical). Finish programming on all preset stations.

Not Complete | Chris Purpura | Theatrical Lighting
Plan: 2-TL2-11B1 - FLOOR PLAN - MAIN LEVEL - UNIT B-1
Created 10-10-2025

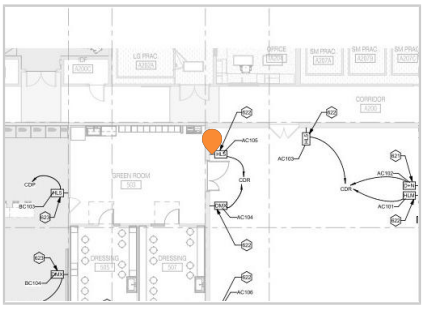


Task messages (time in CDT)

Chris Purpura	Install plates on all HL presets in auditorium (typical). Finish programming on all preset stations. ETC - Complete	10 Oct 06:19 PM

#26 - Finish testing on relocated NET device.

Not Complete | Chris Purpura | Theatrical Lighting
Plan: 2-TL2-11B1 - FLOOR PLAN - MAIN LEVEL - UNIT B-1
Created 10-10-2025

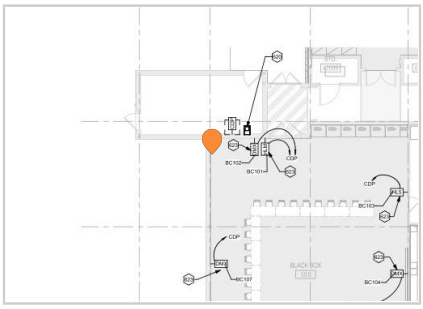


Task messages (time in CDT)

Chris Purpura	Finish testing on relocated NET device.	ETC - Complete	10 Oct 06:23 PM

#27 - Existing preset stations not preset. Key switches in place that are not installed part of the architectural lighting system. Finish installation & programming.

Not Complete | Chris Purpura | Theatrical Lighting
Plan: 2-TL2-11B2 - FLOOR PLAN - MAIN LEVEL - UNIT B-2
Created 10-10-2025

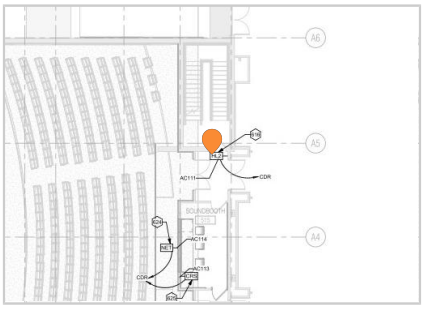

Task messages (time in CDT)

Chris Purpura — 10 Oct 06:26 PM




Chris Purpura — 10 Oct 06:29 PM

Existing preset stations not preset. Key switches in place that are not installed part of the architectural lighting system. Finish installation & programming.

ETC - These are not ETC controls.

#28 - Existing preset stations not preset. Key switches in place that are not installed part of the architectural lighting system. Finish installation & programming.

Not Complete | Chris Purpura | Theatrical Lighting
Plan: 2-TL2-11B2 - FLOOR PLAN - MAIN LEVEL - UNIT B-2
Created 10-10-2025

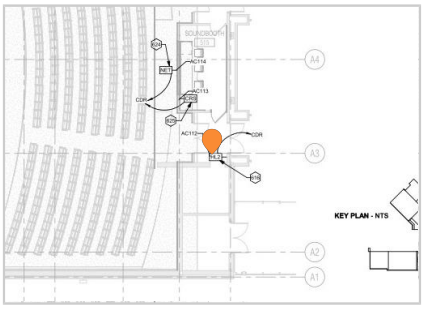


Task messages (time in CDT)

Chris Purpura	Existing preset stations not preset. Key switches in place that are not installed part of the architectural lighting system. Finish installation & programming. ETC - These are not ETC controls.	10 Oct 06:30 PM

#29 - Console fader wing is damaged. Replace & confirm prog ramming.

Not Complete | Chris Purpura | Theatrical Lighting
Plan: 2-TL2-11B2 - FLOOR PLAN - MAIN LEVEL - UNIT B-2
Created 10-10-2025

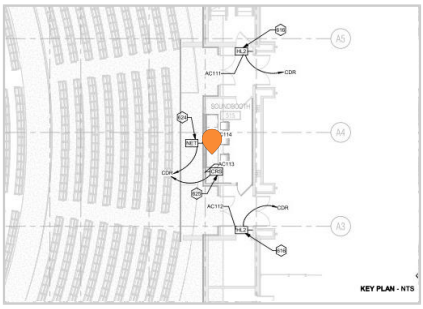


Task messages (time in CDT)

Chris Purpura	Console fader wing is damaged. Replace & confirm programming.	10 Oct 06:30 PM

ETC - Infinity to resolve

#30 - Remove zip ties. Provide tie line on Electrics.

Not Complete | Chris Purpura | Theatrical Lighting
Plan: 2-TL2-11B1 - FLOOR PLAN - MAIN LEVEL - UNIT B-1
Created 10-10-2025

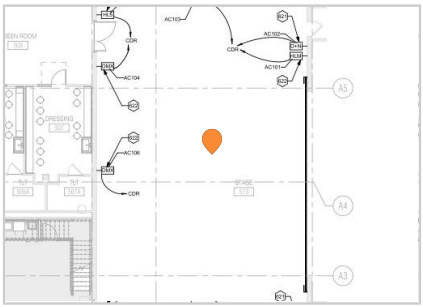


Task messages (time in CDT)

Chris Purpura	Remove zip ties. Provide tie line on Electrics.		10 Oct 06:32 PM
Chris Purpura	Provide adaptors for worklights.		10 Oct 06:33 PM
Chris Purpura	Provide circuit labels on both sides of the connector strip.	ETC - Complete	10 Oct 07:10 PM
Chris Purpura	Provide and set-up portable HLM.	ETC - Complete	10 Oct 07:18 PM

#31 - Set-up and install ETCpad for use.

Not Complete | Chris Purpura | Theatrical Lighting
Plan: 2-TL2-11B1 - FLOOR PLAN - MAIN LEVEL - UNIT B-1
Created 10-10-2025

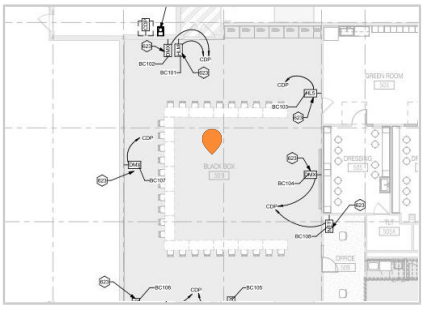


Task messages (time in CDT)

Chris Purpura	Set-up and install ETCpad for use.	ETC - Complete	10 Oct 07:16 PM
Chris Purpura	Finish set-up of HLM.		10 Oct 07:18 PM

#32 - Finish labeling of CDR rack and match as-builts.

Not Complete | Chris Purpura | Theatrical Lighting
Plan: 2-TL2-21B1 - FLOOR PLAN - FA MEZZANINE LEVEL - UNIT B-1
Created 10-10-2025

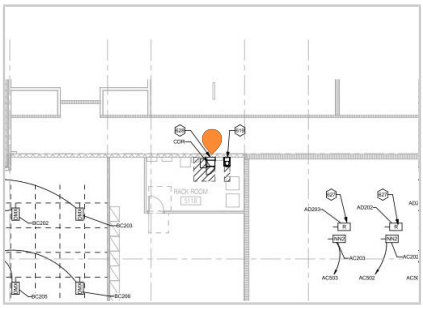

Task messages (time in CDT)

Chris Purpura	Finish labeling of CDR rack and match as-builts.	ETC - Complete	10 Oct 07:20 PM

#34 - Finish installing plates & preset programming.

Not Complete | Chris Purpura | Theatrical Lighting
Plan: 2-TL2-11C1 - FLOOR PLAN - LOWER LEVEL - UNIT C-1
Created 10-11-2025



Task messages (time in CDT)

Chris Purpura




11 Oct 10:09 AM

Chris Purpura — Finish installing plates & preset programming. ETC - Complete — 11 Oct 10:10 AM

Theatrical Rigging

#8 - Video Studio Pipe Grid

Not Installed | Alex Robertson | Theatrical Rigging
Plan: 2-TR2-11C1 - FLOOR PLAN - LOWER LEVEL - UNIT C-1
Created 07-22-2025

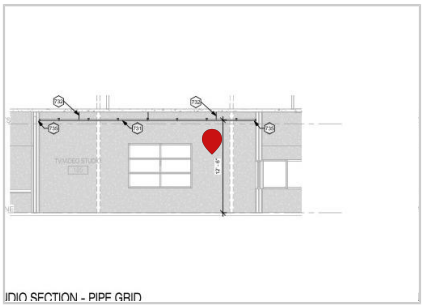


Task messages (time in CDT)

Alex Robertson	Pipe grid was not installed. there are obstructions in the room that prevent the pipe grid from being installed at 12'-6". We have requested the pipe grid be mounted at 11'-0" to allow the proper space for pipe mounted devices.	22 Jul 10:44 AM

#11 - MCC

Not Complete | Paul Brunner | Theatrical Rigging
Plan: 2-TR2-11B2 - FLOOR PLAN - UPPER LEVELS - UNIT B-1
Created 10-10-2025

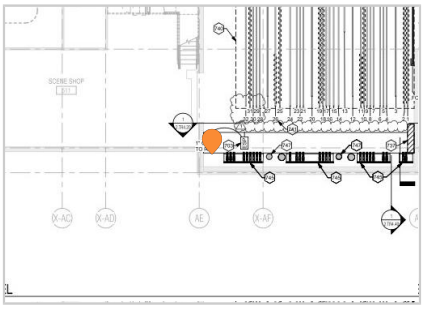


Task messages (time in CDT)

Paul Brunner		10 Oct 09:48 AM
Paul Brunner	Label for motor control cabinet not filled out and not mounted to cabinet.	10 Oct 09:49 AM
Paul Brunner		10 Oct 09:51 AM

#12 - Grid Iron Level

Not Complete | Paul Brunner | Theatrical Rigging
Plan: 2-TR2-11B2 - FLOOR PLAN - UPPER LEVELS - UNIT B-1
Created 10-10-2025

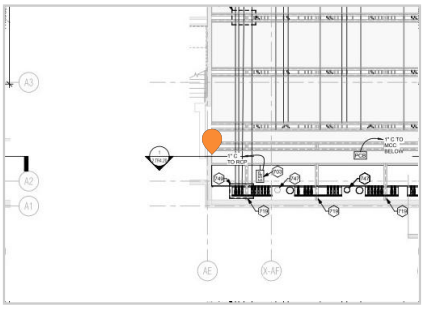


Task messages (time in CDT)

Paul Brunner		10 Oct 09:53 AM
Paul Brunner	Switch at top of ladder at Gridiron level, cover missing.	10 Oct 09:54 AM

#14 - Grid Iron level - Motors

Not Complete | Paul Brunner | Theatrical Rigging
Plan: 2-TR2-11B2 - FLOOR PLAN - UPPER LEVELS - UNIT B-1
Tags: #4
Created 10-10-2025

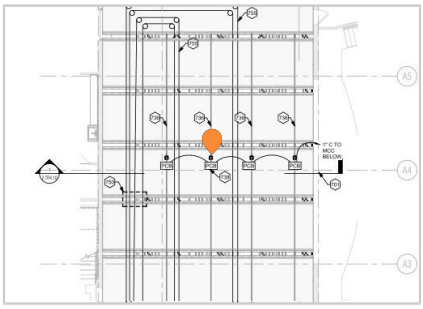

Task messages (time in CDT)

Paul Brunner — 10 Oct 09:55 AM




Paul Brunner — 10 Oct 09:56 AM



Paul Brunner — Lineshaft Hoists: Wire for secondary brake laying on grid. Dress wire to strut backbone per hoist to protect wire. — 10 Oct 09:57 AM

Paul Brunner — 10 Oct 09:57 AM

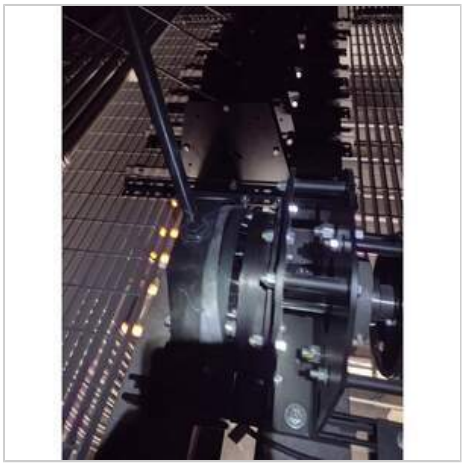

Paul Brunner — #4 Electric Hoist: protective rubber boot not covering brake. Adjust rubber boot to protect brake assembly. — 10 Oct 09:58 AM


Paul Brunner

10 Oct 09:59 AM



#15 - Grid iron Level

Not Complete | Paul Brunner | Theatrical Rigging
Plan: 2-TR2-11B2 - FLOOR PLAN - UPPER LEVELS - UNIT B-1
Created 10-10-2025

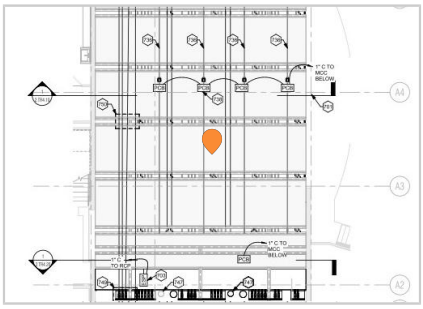

Task messages (time in CDT)

Paul Brunner



10 Oct 10:00 AM

Paul Brunner



10 Oct 10:00 AM

Paul Brunner



10 Oct 10:00 AM

Paul Brunner

Remove all debris from Gridiron and Rigging Gallery levels.

10 Oct 10:01 AM

Paul Brunner



10 Oct 10:02 AM


Paul Brunner

New specified drapery not on site and not installed.

10 Oct 10:03 AM

#19 - Theatrical Battens

Not Complete | Paul Brunner | Theatrical Rigging
Plan: 2-TR2-11B2 - FLOOR PLAN - UPPER LEVELS - UNIT B-1
Created 10-10-2025

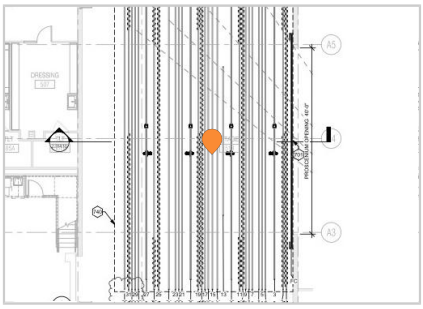

Task messages (time in CDT)

Paul Brunner — 10 Oct 10:30 AM



Paul Brunner — 10 Oct 10:30 AM



Paul Brunner — 10 Oct 10:30 AM



Paul Brunner		10 Oct 10:30 AM
Paul Brunner	Batten splice bolts missing or not properly installed.	10 Oct 10:47 AM
Paul Brunner	Batten end caps not labeled with lineset number or lineset capacity. Centerline marking missing on all battens.	10 Oct 10:48 AM

#20 - New drapery was not on site and not installed.

Not Complete | Paul Brunner | Theatrical Rigging
Plan: 2-TR2-11B1 - FLOOR PLAN - MAIN LEVEL - UNIT B-1
Created 10-10-2025



Task messages (time in CDT)

Paul Brunner	New drapery was not on site and not installed.	10 Oct 10:49 AM

#21 - General TR Items

Not Complete | Jeff Mabray | Theatrical Rigging
Plan: 2-TR2-11B1 - FLOOR PLAN - MAIN LEVEL - UNIT B-1
Tags: #tr_checklist
Created 10-10-2025




Checklist

- [ ] Provide all Owner Training as specified in Contract Documents. (@JMA)
- [ ] Provide documentation of training activities as specified in contract documents. (@JMA)
- [ ] Clean and remove all construction debris. (@JMA)
- [ ] Provide owner signed document acknowledging acceptance of all loose turnover gear. (@JMA)
- [ ] Provide as-built drawings for review as described in the specification. (@JMA)
- [ ] Clean and brush all drapery. (@JMA)

#16 - Lock Rail

Incorrect | Paul Brunner | Theatrical Rigging
Plan: 2-TR2-11B1 - FLOOR PLAN - MAIN LEVEL - UNIT B-1
Created 10-10-2025

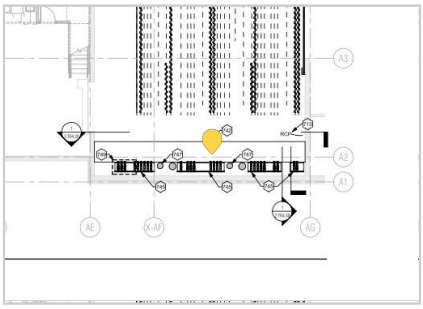


Task messages (time in CDT)

Paul Brunner		10 Oct 10:05 AM
Paul Brunner	Hand line tensioning floor blocks up against rope lock. Tension floor blocks shall 'float" appr oximately mid-way between the floor and bottom arbor stop for proper operation and line tension.	10 Oct 10:08 AM
Paul Brunner	No lineset numbers preset at lock rail.	10 Oct 10:14 AM

#18 - Fire Curtain

Incorrect | Paul Brunner | Theatrical Rigging
Plan: 2-TR2-11B1 - FLOOR PLAN - MAIN LEVEL - UNIT B-1
Created 10-10-2025

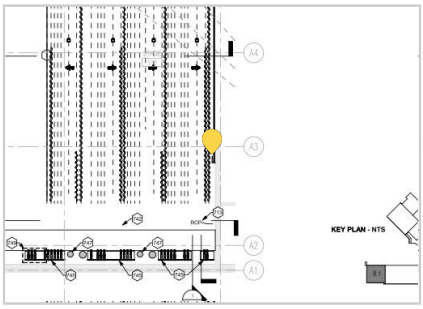

Task messages (time in CDT)

Paul Brunner — 10 Oct 10:24 AM




Paul Brunner — Guide wire for Fire Curtain not adequately mounted to stage floor. Floor piece lifting up. — 10 Oct 10:25 AM

Video Production

#3 - PFP Device Not Installed

Not Installed | Alex Robertson | Video Production
Plan: 2-AV2-11C1 - FLOOR PLAN - LOWER LEVEL - UNIT C-1
Tags: #not_complete:_device,_cabling,_backbox_and_pathway_not_installed
Created 07-22-2025

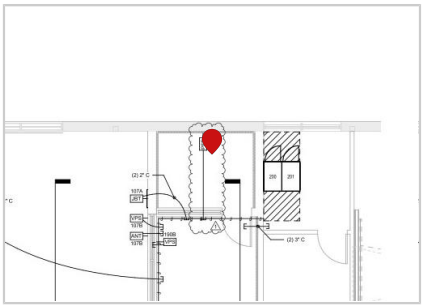

Task messages (time in CDT)


Alex Robertson

22 Jul 10:20 AM



#4 - AV Racks Not Installed


Not Installed | Alex Robertson | Video Production
Plan: 2-AV2-11C1 - FLOOR PLAN - LOWER LEVEL - UNIT C-1
Tags: #not_complete:_device_not_installed
Created 07-22-2025

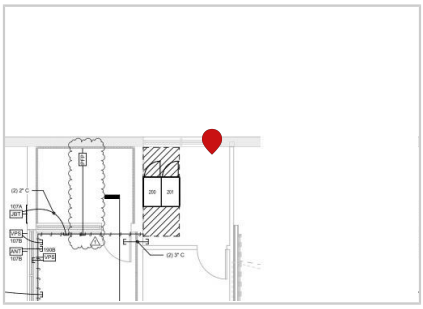

Task messages (time in CDT)


Alex Robertson

22 Jul 10:22 AM

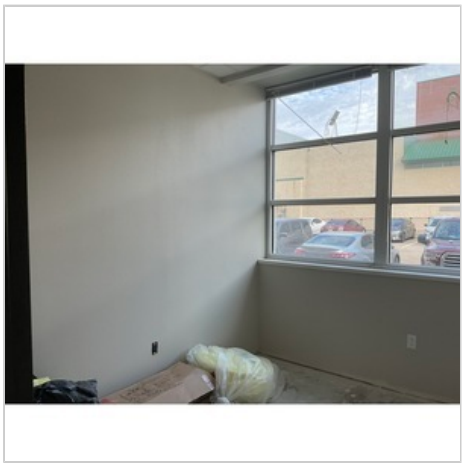

#5 - Electrical outlet installed at wrong height

Incorrect | Alex Robertson | Video Production
Plan: 2-AV2-11C1 - FLOOR PLAN - LOWER LEVEL - UNIT C-1
Tags: #incorrect:_incorrect_placement
Created 07-22-2025

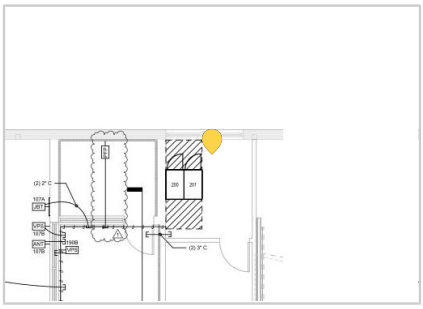


Task messages (time in CDT)

Alex Robertson	Electrical outlet installed at wrong height	22 Jul 10:23 AM
Alex Robertson	L5-20 receptacle should be mounted above the AV rack for this room. Same for other L5-20 receptacle on wall with door.	22 Jul 10:26 AM

#7 - JBE back box not as specified

Incorrect | Alex Robertson | Video Production
Plan: 2-AV2-11C1 - FLOOR PLAN - LOWER LEVEL - UNIT C-1
Tags: #incorrect:_incorrect_product_installed
Created 07-22-2025

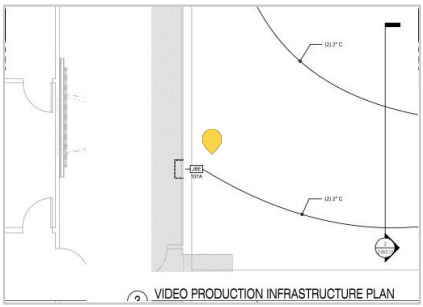

Task messages (time in CDT)

Alex Robertson	Contractor installed incorrect back box. The faceplate will not fit installed back box	22 Jul 10:40 AM
Alex Robertson	To get systems ready for the first of school, the contractor is going to trim faceplate and move receptacles around. They will replace with properly sized faceplate once it's available.	22 Jul 10:41 AM
